

RAILROAD COMMISSION OF TEXAS

CHRISTI CRADDICK, *CHAIRMAN*
RYAN SITTON, *COMMISSIONER*
WAYNE CHRISTIAN, *COMMISSIONER*

INTERNAL
OIL AND GAS DIVISION
CLAY WOODUL
ASSISTANT DIRECTOR, FIELD OPERATIONS

MEMORANDUM

TO: Chairman Christi Craddick
Commissioner Ryan Sitton
Commissioner Wayne Christian ^{ds}

THROUGH: Wei Wang, Executive Director ^{WOW}
Danny Sorrells, Assistant Executive Director ^{DS}
Director, Oil and Gas Division ^{DS}

FROM: Clay Woodul, Assistant Director ^{CW}
Field Operations ^{ds}

DATE: November 16, 2020

SUBJECT: Oil Field Cleanup Program Quarterly Status Report, Fiscal Year 2020, 4th Quarter


Well Plugging: The 4th quarter performance for State-Managed Plugging includes 445 wells plugged with a total expenditure of \$9,006,382.25 using Oil and Gas Regulation and Cleanup (OGRC) and Economic Stabilization funds. This includes wells that have been physically plugged, invoiced by the plugging contractor, and approved for payment by Field Operations. Additionally, during the 4th quarter, 566 wells were approved for plugging with State funds. A total of 1498 wells were physically plugged through the end of the 4th quarter, of which, 1477 have been invoiced and paid. The actual wells plugged and expenditure by district for fiscal years 2018, 2019 and 2020 and the well plugging goals and budgets by district for fiscal year 2020 are shown on the attached graphs. The fiscal year 2020 budget is \$42,281,610.

Site Remediation: The 4th quarter performance for Site Remediation includes 67 cleanup activities completed with total expenditure of \$6,411,753.00 using OGRC funds. There were three activities completed with expenditure of \$62,769.00 using Grant Funds. During the 4th quarter 35 cleanup activities were authorized for cleanup with State funds. Site Remediation has completed and formally closed a total of 253 cleanup activities using OGRC funds and five activities with Grant Funds for a total of 258 completed activities during fiscal year 2020. The actual remediation activities and expenditure by district for fiscal years 2018, 2019, and 2020 and the goals for the Site Remediation activities by district for fiscal year 2020 are shown on the attached graphs. The fiscal year 2020 budget is \$17,150,000.00.

KCW
Attachments:


cc Wei Wang, Executive Director
Danny Sorrells, Director, Oil & Gas Division
Peter G. Pope, P.G., Manager, Site Remediation

**Field Operations/Well Plugging
Oil Field Cleanup Program
4th Quarter FY 2020
Wells Plugged
FY 18 Actual, FY 19 Actual, FY 20 Actual, FY 20 Plugging Goal**

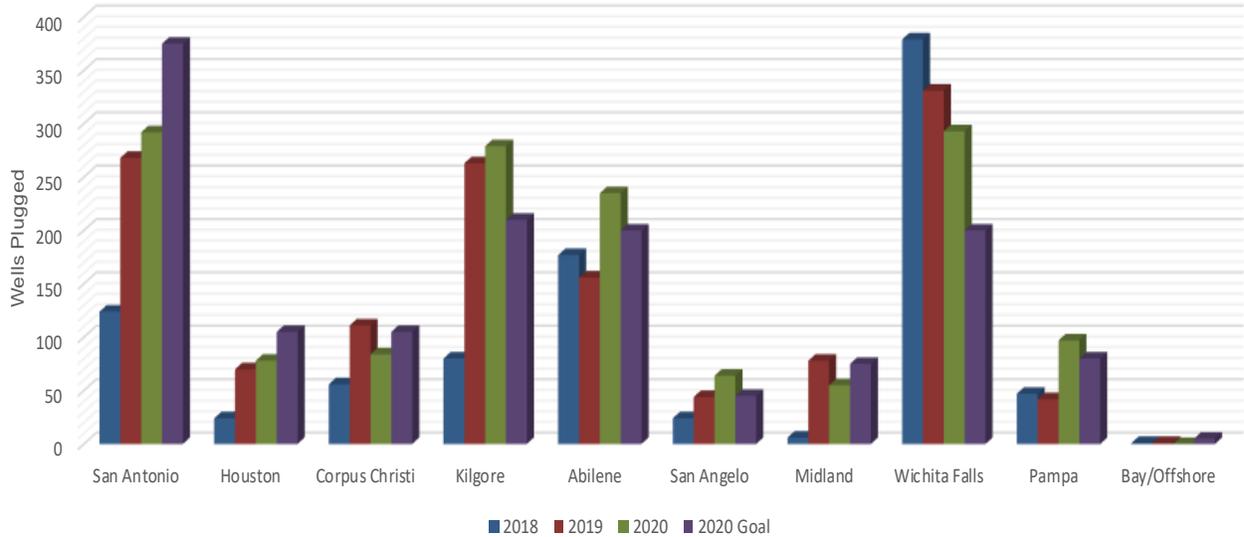


	San Antonio	Houston	Corpus Christi	Kilgore	Abilene	San Angelo	Midland	Wichita Falls	Pampa	Bay/Offshore	Total
2018	124	24	56	80	177	24	6	379	47	1	918
2019	268	70	111	263	156	44	78	331	42	1	1,364
2020	292	78	84	279	235	64	55	293	97	0	1,477
2020 Goal	375	105	105	210	200	45	75	200	80	5	1,400

**Field Operations/Well Plugging
Oil Field Cleanup Program
4th Quarter FY 2020
Plugging Expenditures
FY 18 Actual, FY 19 Actual, FY 20 Actual**

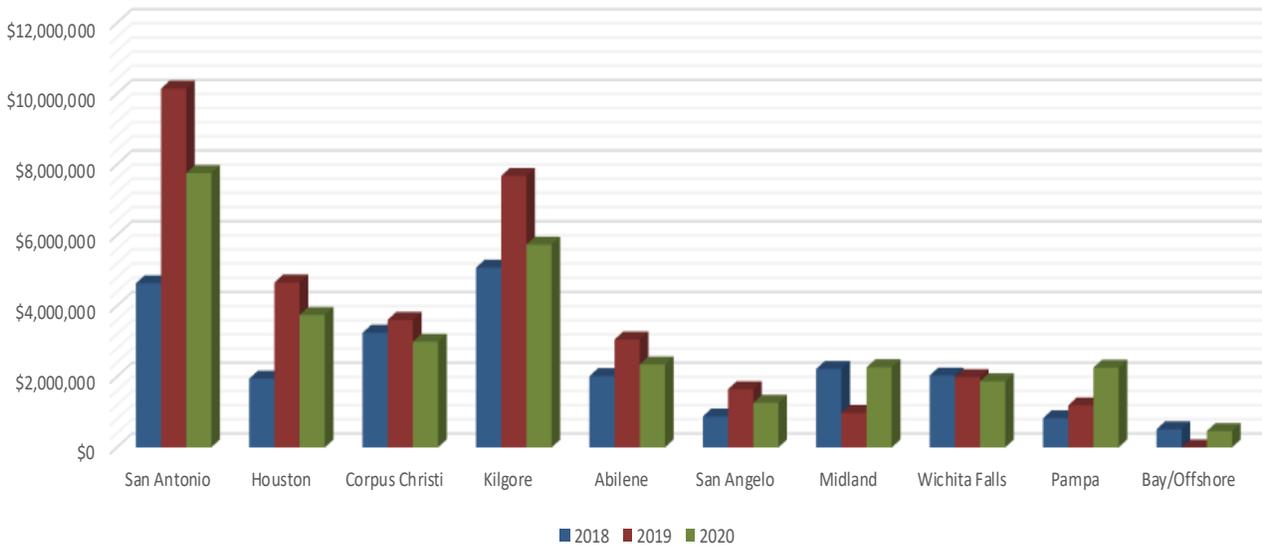


	San Antonio	Houston	Corpus Christi	Kilgore	Abilene	San Angelo	Midland	Wichita Falls	Pampa	Bay/Offshore	Total
2018	\$4,638,511	\$1,942,826	\$3,242,116	\$5,084,697	\$2,017,215	\$876,051	\$2,220,120	\$2,034,806	\$823,816	\$512,944	\$23,393,101
2019	\$10,144,871	\$4,663,341	\$3,609,920	\$7,677,324	\$3,049,846	\$1,643,641	\$978,472	\$1,988,958	\$1,186,538	\$0	\$34,942,911
2020	\$7,756,313	\$3,745,634	\$2,991,893	\$5,733,525	\$2,346,967	\$1,263,536	\$2,270,225	\$1,871,546	\$2,255,940	\$465,364	\$30,700,942

**Site Remediation
Oil Field Cleanup Program
4th Quarter FY 2020
Activities Completed
FY 18 Actual, FY 19 Actual, FY20 Actual FY20 Goal**

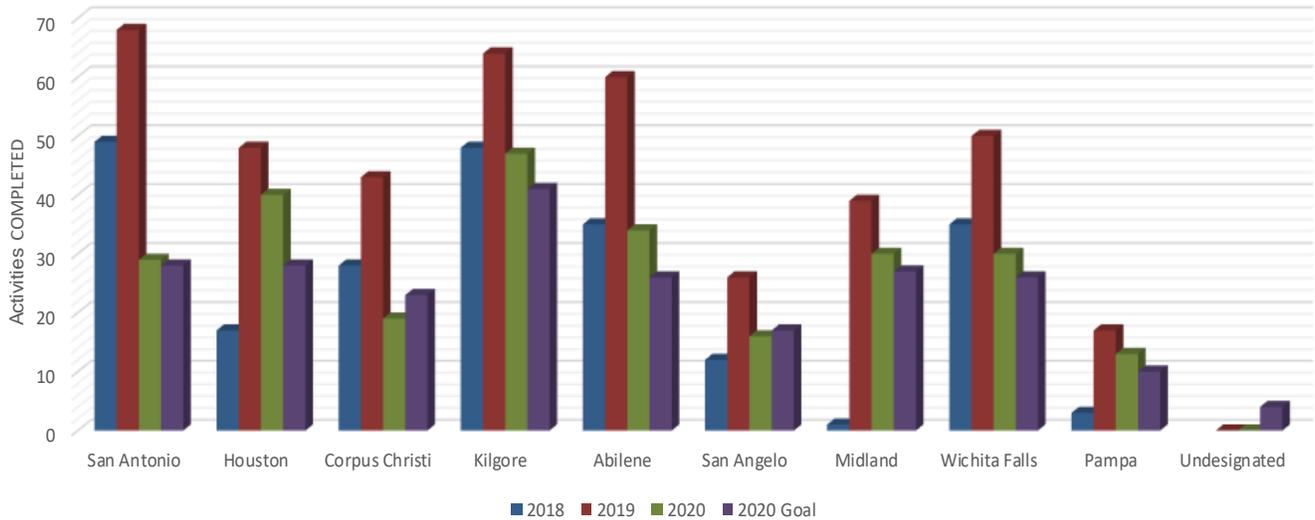

	San Antonio	Houston	Corpus Christi	Kilgore	Abilene	San Angelo	Midland	Wichita Falls	Pampa	Undesignated	Total
2018	49	17	28	48	35	12	1	35	3		228
2019	68	48	43	64	60	26	39	50	17	0	415
2020	29	40	19	47	34	16	30	30	13	0	258
2020 Goal	28	28	23	41	26	17	27	26	10	4	230

**Site Remediation
Oil Field Cleanup Program
4th Quarter FY 2020
Cleanup Expenditures
FY 18 Actual, FY 19 Actual, FY 20 Actual**

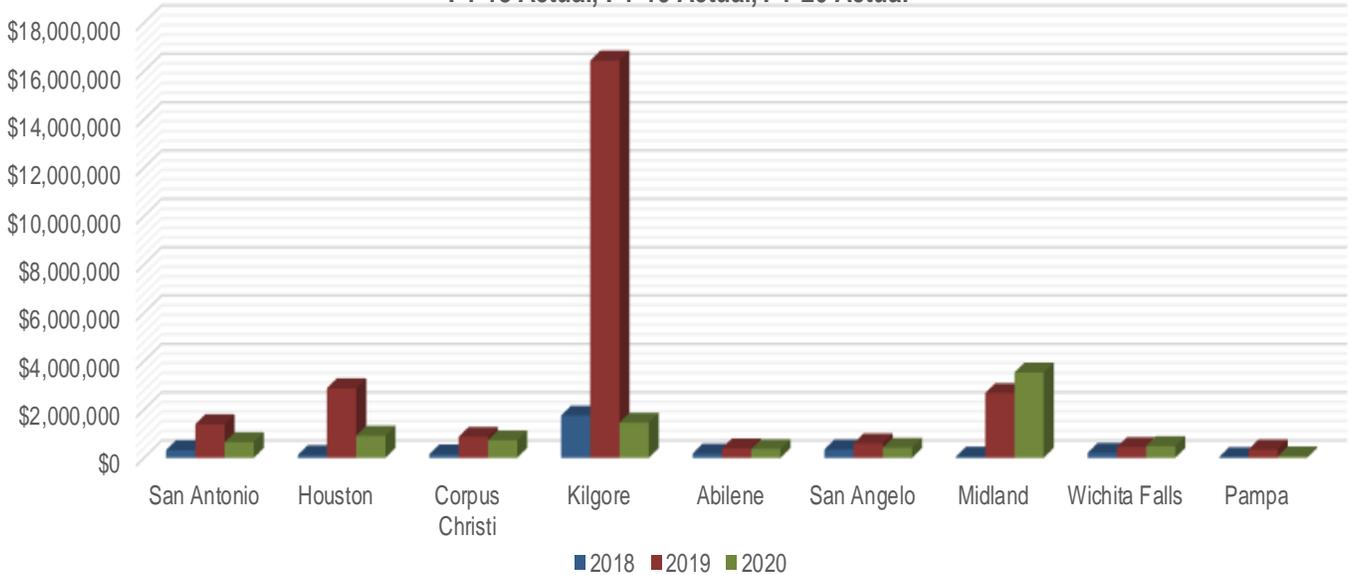

	San Antonio	Houston	Corpus Christi	Kilgore	Abilene	San Angelo	Midland	Wichita Falls	Pampa	Undesignated	Total
2018	\$321,045	\$109,308	\$146,630	\$1,747,707	\$177,386	\$347,172	\$46,798	\$204,855	\$36,189		\$3,137,090
2019	\$1,393,443	\$2,881,457	\$869,979	\$16,436,316	\$394,704	\$601,286	\$2,677,616	\$448,824	\$349,689	\$0	\$26,053,314
2020	\$649,963	\$920,498	\$728,001	\$1,455,227	\$366,017	\$417,384	\$3,528,903	\$486,928	\$64,845	\$0	\$8,617,766
